




RIPPŌTAI

HOW WE WORK

OUR PROCESS, FROM FIRST CALL TO HANDOVER



The approach

Four things hold every Rippotai project together. Everything that follows is a consequence of them.

One point of contact

You speak to the Project Lead, start to finish
No chasing five people for one answer
Decisions confirmed in writing, on one channel

Sign-off before spend


Nothing ordered before you approve it
Nothing cut or installed before the gate clears
Changes quoted in writing, first

Nothing hidden in the BOQ

Every item priced line by line
No lump sums, no allowances
Brands and quantities named upfront

Payment follows progress

Milestones release against stages of work
Never against calendar dates
The final share is retained until snags close

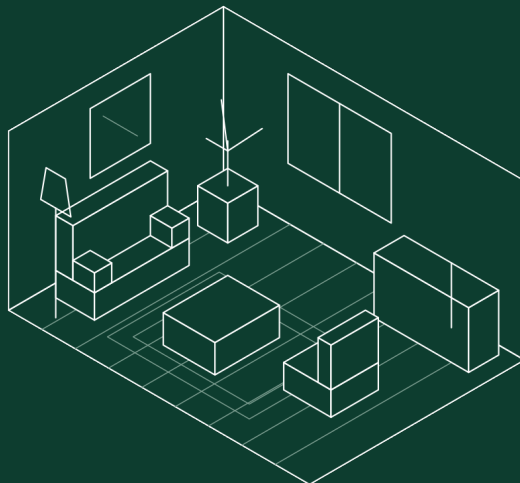

How a project runs

01 Discovery

Site visit, measurements and photographs
Requirement brief and lifestyle notes
You share references and a budget range

05 Execution

Seven phases, sequenced at site
Daily photo reporting, weekly walkthrough
You approve each stage sign-off

02 Design

Layout options and circulation study
3D views and a finish direction
You approve concept and layout

06 Snagging

Joint walkthrough, room by room
Every item recorded in writing
You mark what needs fixing

03 Estimate


A BOQ priced line by line
Brands, quantities and specifications named
You approve cost and scope

07 Handover

Deep clean and final walkthrough
Drawings, warranties, manuals and keys
You confirm snag closure

04 Agreement

Payment schedule, timeline and terms
Scope of Work signed alongside
You sign and release the advance

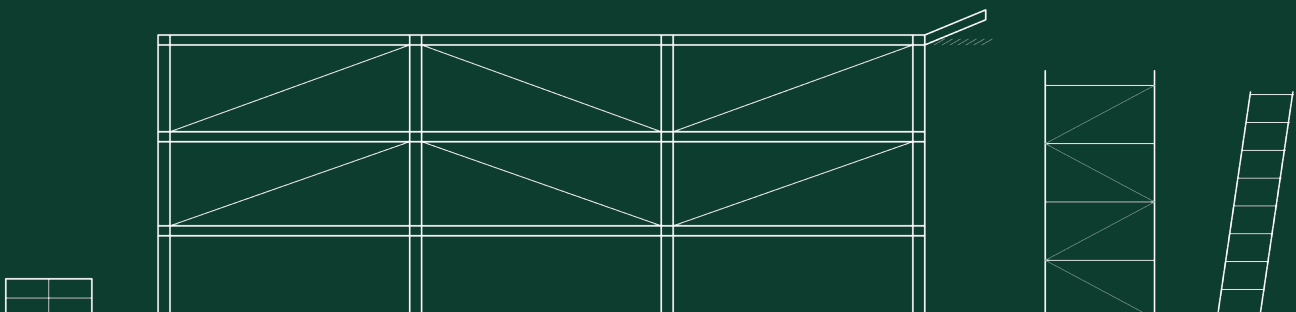

Who you deal with

Principle Architect

Sagar Chhabra
Design direction and drawings
Final approvals on every gate

Site Supervisor

On site every working day
Labour control and sequencing
Quality checks before each stage closes

Project Lead

Sarathi Jangra
Your single point of contact
Timeline, coordination and reporting

Admin Coordinator

Billing, documents and scheduling
Material tracking and delivery notes
Vendor paperwork and warranties

WHAT YOU RECEIVE, AND WHEN

Daily

Site photo report on WhatsApp
Labour count and work done

Monthly


Stage note and billing
Revised timeline if anything moved

Weekly

Progress walkthrough
Upcoming selections flagged

At each gate

Written approval request
Drawings or samples attached



Ground rules

Six things we ask of you. They exist so the timeline holds and the cost stays where it was agreed.

One channel

Decisions are confirmed in writing
Verbal instructions at site are not actionable

Site access

Water, power, storage and lift access
Society permissions before mobilisation

Decisions within 48 hours

Selections held longer push the phase
The timeline moves with it, day for day

Changes are quoted first

Written cost and time impact
Billed in advance of procurement

No work without approval

Nothing ordered, cut or installed
Before the relevant gate is signed

Snags close in writing

Handover against a signed snag sheet
Never a verbal confirmation

This document sets out how we work and applies to every Rippotai project. What is being built, what it costs and when it completes are recorded separately in the Scope of Work, the Payment Schedule and the Plan of Action.



RIPPOTAI

ARCHITECTURE · INTERIORS · TURNKEY

