




RIPPŌTAI

BUSINESS PROPOSAL

INTERIOR DESIGN & TURNKEY EXECUTION
PINK APPARTMENT · 49 PINK APPARTMENT, PASCHIM VIHAR

PREPARED FOR · _____

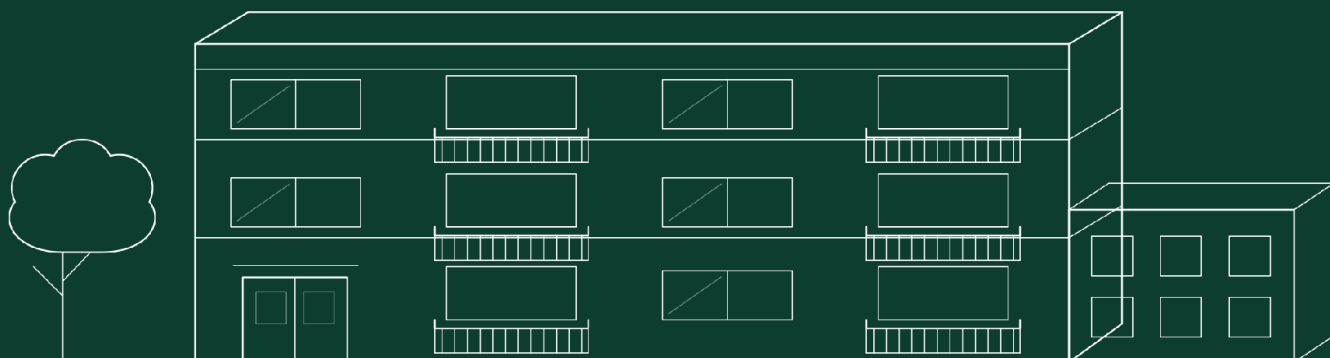


Contents

01	Welcome note	Why we are the right team for this
02	Project detail	The unit, the brief and the engagement
03	Scope of work	What is included, and what is not
04	How we work	Our process, from first call to handover
05	Plan of action	Seven phases across four to five months
06	Budget estimate	Indicative cost, discipline by discipline
07	Payment schedule	Seven milestones against stages of work
08	Next steps	What happens after you say yes

This proposal is valid for thirty days from the date of issue. Figures are indicative until the BOQ is frozen and the Agreement is signed.

01 Welcome note

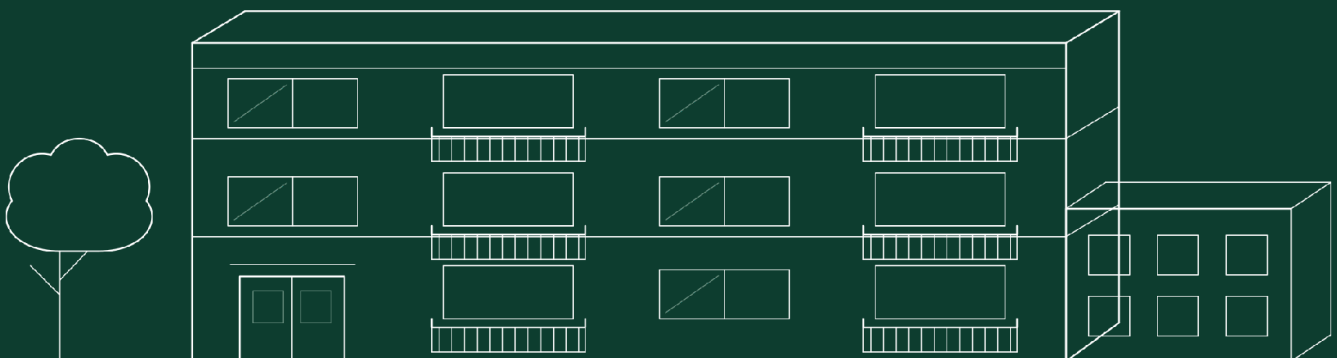

01 Welcome note

Thank you for inviting Rippotai to work on your home at Paschim Vihar.

This proposal sets out everything you need to make a decision — what we will build, how we will run the site, how long it takes, what it costs, and when each payment falls due. Nothing is held back for later.

We work as a single accountable team. One Project Lead owns your project end to end, one BOQ prices every item line by line, and one schedule ties payment to visible stages of work rather than to calendar dates. You will never be asked to release money for something you cannot see.

Rippotai is the architecture and turnkey arm of SP Syndicate, working across Delhi NCR on residential and commercial interiors. We design it, we cost it honestly, and we build it ourselves — which means no gap between the drawing you approve and the room you walk into.

WHAT THIS PROPOSAL COVERS

Project detail and engagement type
Scope of work, discipline by discipline
Our process and where you sign off
Phase plan and timeline


AND

Indicative budget estimate
Payment milestones and terms
What happens next, and when
Who to speak to at every stage

Sagar Chhabra

Principle Architect · Rippotai

02 Project Detail

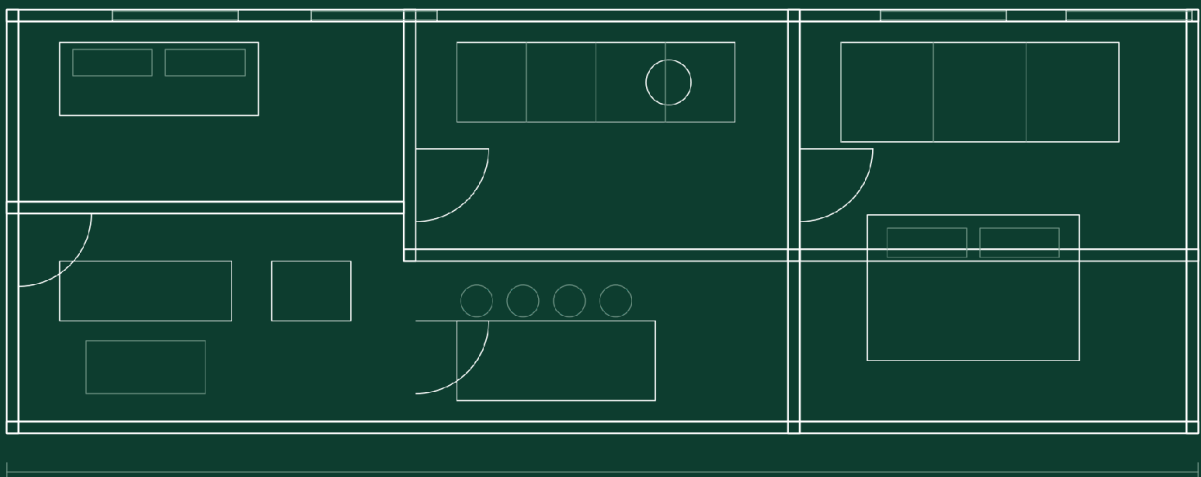

02 Project detail

Project name	Client name
Site address	Total area (sq ft)
Unit type	Built-up area (sq ft)
Carpet area (sq ft)	Bathrooms
Bedrooms	Date of issue
Prepared by	Reviewed by

PROJECT TYPE

- ☐ Residential
- ☐ Commercial
- ☐ Industrial
- ☐ Hospitality
- ☐ Institutional

Work type

☐ Consultancy

Design, drawings and specifications
Vendor tendering and rate comparison
Periodic site visits and quality checks
Execution contracted by the Client


☐ Turnkey execution

Everything under consultancy, plus
Procurement, labour and site management
Single-point delivery against a signed BOQ
Handover with warranties and as-built drawings

THE BRIEF IN ONE PARAGRAPH

CONSTRAINTS AND SITE CONDITIONS NOTED

03 Scope of Work

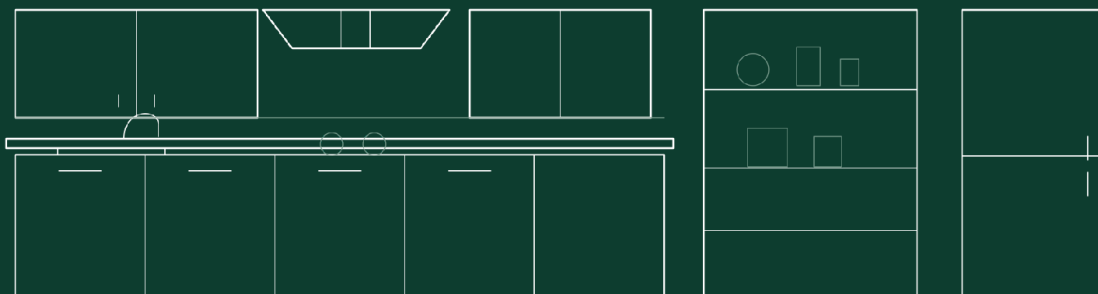

03 Scope of work

INCLUDED

Site supervision and skilled labour
Material procurement and delivery
All drawings up to GFC stage
Vendor selection and coordination
Debris removal and deep cleaning
Twelve-month workmanship cover

NOT INCLUDED

Society and authority approvals
Structural changes to the building
Electrical load enhancement
Appliances not listed in the BOQ
Curtains, art and styling accessories
GST and statutory levies

OPTIONAL – QUOTED SEPARATELY

Loose furniture sourcing
Curtains, blinds and sheers
Home automation and smart controls
Profile and cove lighting

Wardrobe internals upgrade
Balcony decking and planters
Appliance supply and installation
Art, decor and styling

SCOPE BY DISCIPLINE

Civil & demolition

Removal, cutting and debris disposal
Masonry, plaster and levelling
Door and window openings

Mill work & joinery

Modular kitchen and wardrobes
Vanities and storage units
Site-fabricated joinery

MEP & waterproofing

Concealed wiring and conduits
AC piping, drainage and plumbing
Wet area and terrace treatment

Paint & polish

Primer, putty and two coats
Wood polish and veneer finish
Touch-ups at snagging

Flooring & tiling

Floor and wall tiling
Counters, skirting and dado
Grouting and edge finishing

Fixtures & fittings

Light fixtures and switches
CP fittings and sanitaryware
Hardware and accessories

Ceiling & POP


Framework and boarding
Cove and profile detailing
Punning and surface preparation

Loose furniture

Sourcing and coordination
Delivery and placement
Optional — if selected

The area-wise scope matrix — every discipline against every space — is issued as a separate annexure and forms part of the Agreement.

04 How we Work

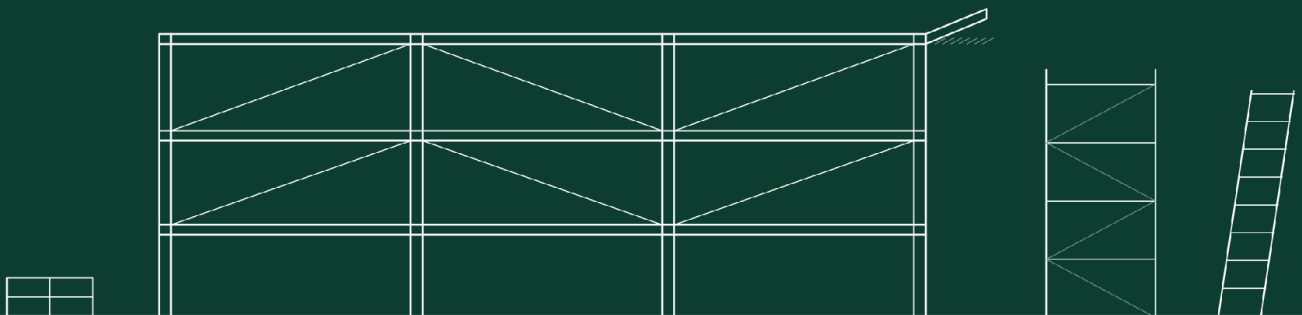

04 How we work

One point of contact

You speak to the Project Lead, start to finish

Decisions confirmed in writing, on one channel

Sign-off before spend

Nothing ordered before you approve it

Changes quoted in writing, first

Nothing hidden in the BOQ

Every item priced line by line

No lump sums, no allowances

Payment follows progress

Milestones release against stages of work

Never against calendar dates

WHO YOU DEAL WITH

Principle Architect

Sagar Chhabra

Design direction and final approvals

Project Lead

Sarathi Jangra

Your single point of contact

Site Supervisor

On site every working day

Labour control and quality checks

Admin Coordinator

Billing, documents and scheduling

Material tracking and warranties

WHERE YOU SIGN OFF

G1 Concept

Layout, look and material direction

G4 Stage

Each of the seven execution phases

G2 BOQ

Cost, scope and quantities frozen

G5 Handover

Snag list closed and signed

G3 GFC

Working drawings and material samples

WHAT YOU RECEIVE, AND WHEN

Daily

Site photo report on WhatsApp

Monthly

Stage note, billing and revised timeline


Weekly

Progress walkthrough with the Project Lead

At each gate

Written approval request with drawings

05 Plan of Action

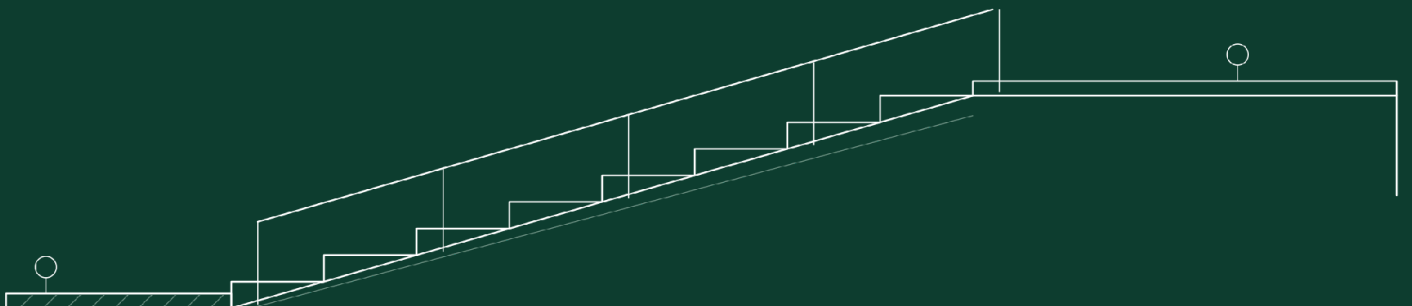



05 Plan of action

Seven phases, sequenced at site. Phases overlap where the trade allows, which is how four to five months of work compresses into the stated programme.

	PHASE	WHAT HAPPENS	DURATION
01	MEP & Waterproofing	Waterproofing of wet areas and terraces, AC piping and ducting, concealed wiring and plumbing lines. PARALLEL – OVERALL MATERIAL SELECTION	30–45 days
02	Tiling & POP	Floor and wall tiling, stone and dado work, POP punning, false ceiling framing and cove detailing. PARALLEL – LOOSE FURNITURE FINALISATION	25–30 days
03	Mill Work & Joinery	Modular kitchen, wardrobes, vanities and site-fabricated mill work, with the first coat of paint. INCLUDES – PAINT 1ST COAT	30–40 days
04	Fixtures & Fittings	Light fixtures, electrical fittings and appliances, CP fittings and sanitaryware, hardware and accessories.	12–15 days
05	Paint & Polish	Final coat on all walls and ceilings, polishing of wood work and veneer, touch-ups and edge finishing.	15–20 days
06	Snagging	Joint walkthrough room by room, written defect list, closure of every recorded item.	7–10 days
07	Handover	Deep clean, final walkthrough, keys, warranty cards and as-built service drawings.	3–5 days
	OVERALL PROGRAMME		4–5 months

Durations run from mobilisation of that phase and assume decisions within forty-eight hours and payments released on time. Statutory construction restrictions and material lead times extend the programme proportionately.

06 Budget Estimate



06 Budget estimate

An indicative range at proposal stage, built from the areas and the finish level discussed. It becomes a firm number when the BOQ is priced line by line and frozen at Gate 02.

HEAD OF COST	AMOUNT (₹)
Civil & demolition Removal, masonry, plaster and making good	
MEP & waterproofing Electrical, plumbing, AC and wet area treatment	
Flooring & tiling Floor, wall, counters and skirting	
Ceiling & POP Framework, boarding and cove detailing	
Mill work & joinery Kitchen, wardrobes, vanities and storage	
Paint & polish Walls, ceilings, wood polish and veneer	
Fixtures & fittings Lighting, CP fittings, sanitaryware and hardware	
Loose furniture & decor Optional – included only if ticked in scope	
Site management & supervision Labour control, logistics and quality checks	
Subtotal	
Contingency Against site conditions found after demolition	
ESTIMATE, EXCLUSIVE OF GST	₹ _____

WHAT THE ESTIMATE ASSUMES

Finish level as discussed at the site visit
Standard ceiling height, no structural change
Material lead times within four weeks
Uninterrupted site access and services
Decisions returned within forty-eight hours

WHAT SITS OUTSIDE IT

GST and statutory levies
Society charges, permissions and deposits
Appliances and loose furniture unless ticked
Client-supplied material and its handling
Variations raised after the BOQ is frozen

HOW THE NUMBER FIRMS UP

01 Estimate

This document – a range, not a quote

03 Freeze at Gate 02

Scope and cost signed, Agreement issued


02 Detailed BOQ

Every item priced, brand and quantity named

04 Variations only

Any change quoted in writing before it is built

07 Payment Schedule

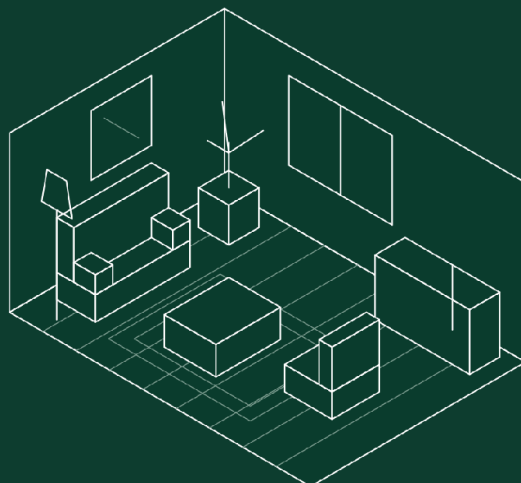

07 Payment schedule

Each milestone falls due before the corresponding phase is mobilised, so material can be ordered and labour deployed without a break between phases.

	MILESTONE	RELEASE TRIGGER	SHARE
M1	Booking & mobilisation	On signing, before site start	15%
M2	MEP & waterproofing	Before Phase 01 mobilises	20%
M3	Tiling & POP	Before Phase 02 mobilises	20%
M4	Mill work & joinery	Before Phase 03 mobilises	20%
M5	Fixtures & fittings	Before Phase 04 mobilises	10%
M6	Paint & polish	Before Phase 05 mobilises	10%
M7	Snagging & handover	On closure of the signed snag list	5%
	TOTAL CONTRACT VALUE		100%

KEY TERMS

Invoicing and due date

Payment due within three working days of invoice

Variations

Quoted in writing, billed 100% in advance

Mode of payment

NEFT, RTGS or cheque to the Rippotai account only

No cash, and no payment to anyone at site

Retention

Final 5% held until the snag list is signed

Taxes

All figures exclusive of GST

Title of materials

Passes to the Client on full milestone payment

Delay in release

Beyond seven days, work may pause


Timeline extends day for day

Jurisdiction

Settled amicably, failing which courts at Delhi

The full sixteen-clause Payment Schedule is issued as a separate document and forms part of the Agreement.

08 Next Steps

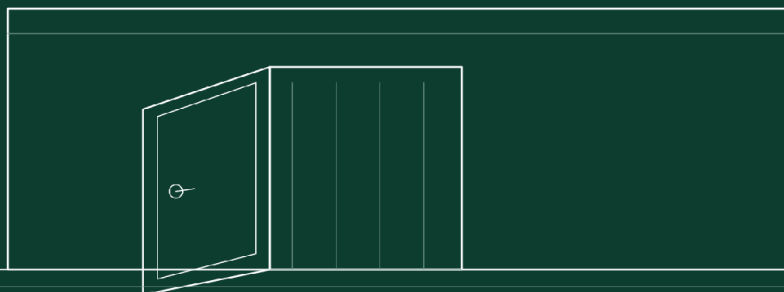

08 Next steps

Five things stand between this proposal and a live site. Most clients clear them inside a fortnight.

01 Review this proposal

Take a week. Mark anything unclear
We will walk it through with you

04 Sign the Agreement

Scope of Work, Payment Schedule, Plan of Action
Issued together for signature

02 Confirm the scope

Tick the engagement and optional items
We revise the BOQ against your ticks

05 Release M1 and mobilise

15% booking and mobilisation
Site team on the ground within five days

03 Freeze cost at Gate 02

BOQ priced line by line and signed
The estimate becomes a firm number

WHAT WE NEED FROM YOU TO START

☐ Signed Scope of Work and Agreement

☐ Booking and mobilisation payment

☐ Society permission for work and material lift

☐ Access, keys and a point of contact at site

☐ Water and power connection at the unit

☐ Any client-supplied material schedule

TALK TO US

Sagar Chhabra

Principle Architect

Design direction and approvals

Sarthi Jangra

Project Lead

Your single point of contact

Rippotai

Architecture · Interiors · Turnkey

Delhi NCR

Proposal validity

Thirty days from date of issue

Rates held for the stated period

The Client confirms having read this proposal and accepts the scope, programme, indicative budget and payment milestones set out in it, subject to the BOQ being frozen and the Agreement signed.

FOR RIPPOTAI

ACCEPTED BY THE CLIENT

Authorised Signatory

Name · Sagar Chhabra

Date · _____

Client Signature

Name · _____

Date · _____
